Solar ESS Co. Ltd.
53 Moo 2 Tambon Nanglae, Amphoe Muang
Chiang Rai 57100, Thailand
Tel 063 151 6694, 089 632 5829
www.solaress.org · LINE: solaress1

SOLAR ESS MONTHLY REPORT · OCTOBER 2026 · SOLISCLOUD · PLANT REPORT


Upgrade opportunity

Forklift workshop, Songkhla


Panels throttled · no daytime load

20 kWp · 20 kW 3-phase hybrid inverter · no battery

546	1.14	76%	7.6	14	0.0
kWh solar	kWh/kWp/day	solar share of use	kWh/day bought	kWh exported	kWh/day from battery

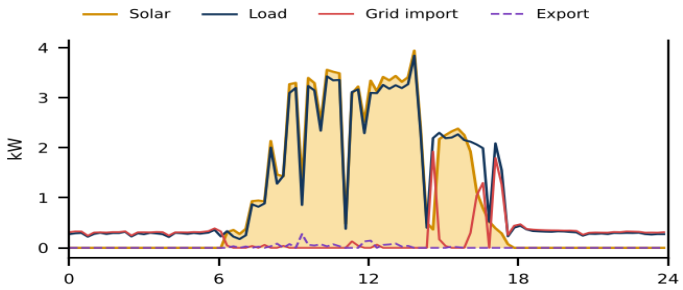

24 October, 5-minute data

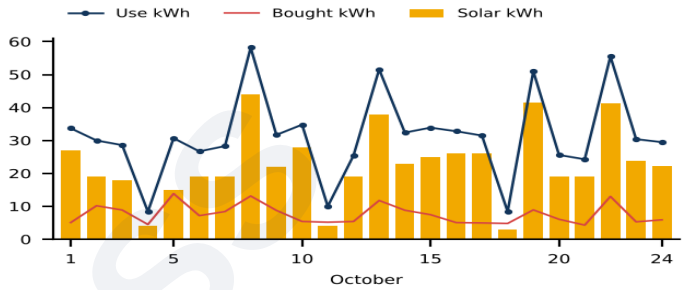

Daily totals, 1–24 October


What we found

• Lowest yield on a 20 kWp system: 1.14 kWh/kWp/day. No battery and zero export, so the inverter only produces what the site uses (3.9 kW peak).
• Site uses only 31 kWh/day; 17 grid under-voltage alarms.

What to do

• Charge forklifts and run compressors between 10:00 and 15:00 to use the free solar.
• A battery is not worth it at today's low grid purchase (8 kWh/day). Check grid voltage because of the under-voltage trips.

How this plant compares with the other SolisCloud plants (kWh per kWp per day, 1–24 Oct)

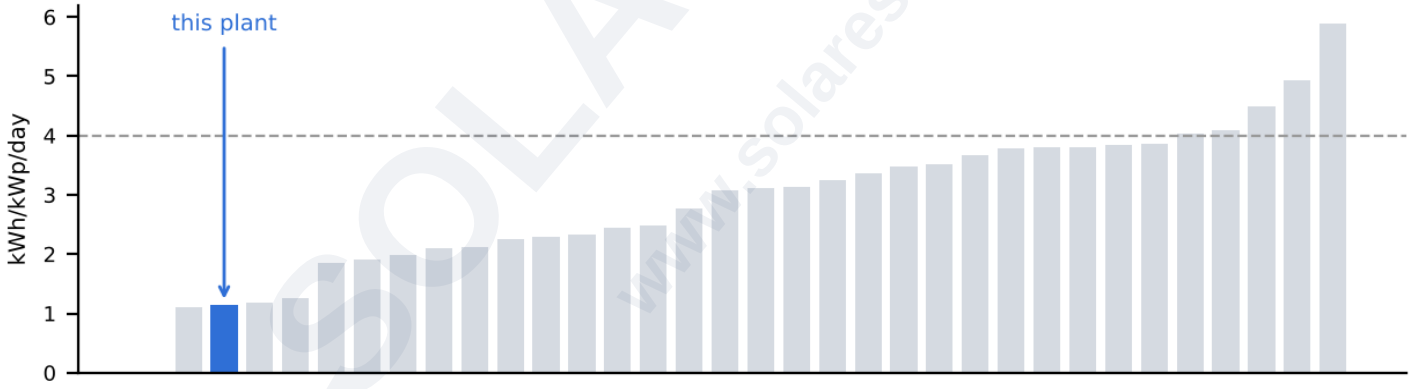

Rank 32 of 34 for yield per kWp. Dashed line ≈ 4.0, a typical clear month in the north and centre. A low yield is not always a fault – a full battery or little daytime load makes the inverter throttle the panels.

This plant report is part of the October 2026 SolisCloud fleet review on www.solaress.org (Technical → Monthly Report), which also lists the recommended standard settings. Figures are estimates from monitoring data; site name removed.
