Solar ESS Co. Ltd.
53 Moo 2 Tambon Nanglae, Amphoe Muang
Chiang Rai 57100, Thailand
Tel 063 151 6694, 089 632 5829
www.solaress.org · LINE: solaress1

SOLAR ESS MONTHLY REPORT · OCTOBER 2026 · SOLISCLOUD · PLANT REPORT


Upgrade opportunity

Home S13, Bangkok


Add battery 20–30 kWh

20 kWp · 20 kW 3-phase hybrid inverter · no battery

1503	3.13	39%	98.4	19	0.0
kWh solar	kWh/kWp/day	solar share of use	kWh/day bought	kWh exported	kWh/day from battery

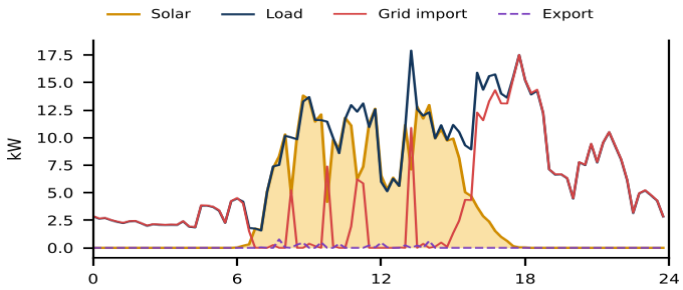

24 October, 5-minute data

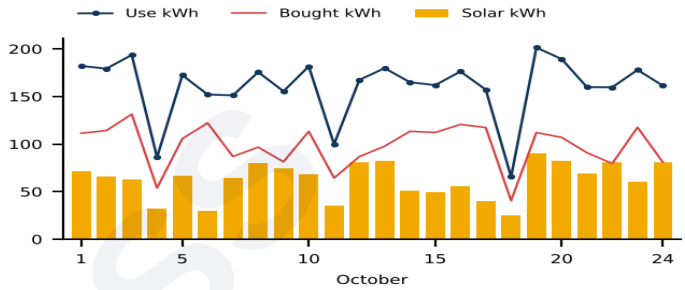

Daily totals, 1–24 October


What we found

• No battery on a hybrid inverter. Evening load 10–17 kW, buying 98 kWh/day.
• Solar 3.1 kWh/kWp/day (Bangkok). 10 grid over-voltage trips in October.

What to do

• Add 20–30 kWh of battery: about 600–900 kWh/month less grid.
• Measure grid voltage at the meter because of the over-voltage trips.

How this plant compares with the other SolisCloud plants (kWh per kWp per day, 1–24 Oct)

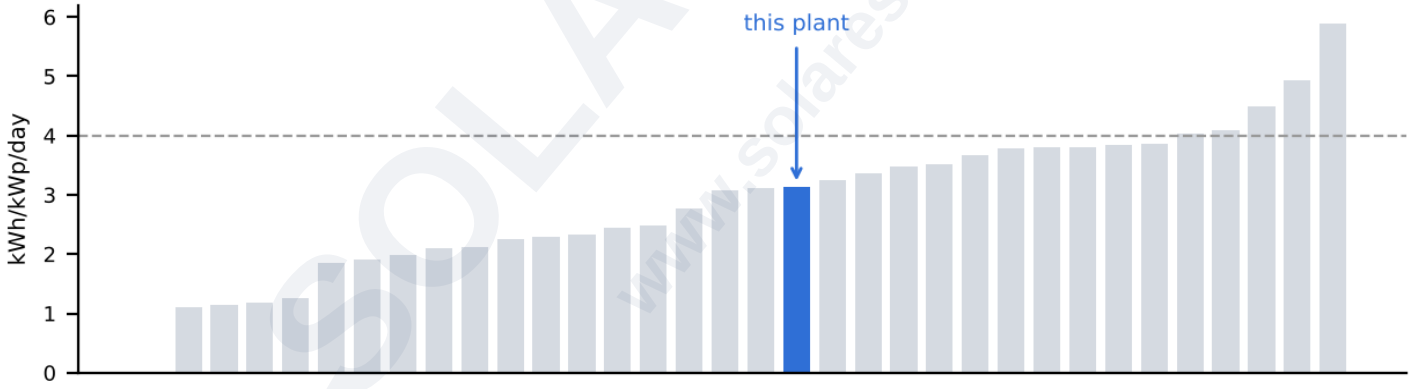

Rank 16 of 34 for yield per kWp. Dashed line ≈ 4.0, a typical clear month in the north and centre. A low yield is not always a fault – a full battery or little daytime load makes the inverter throttle the panels.

This plant report is part of the October 2026 SolisCloud fleet review on www.solaress.org (Technical → Monthly Report), which also lists the recommended standard settings. Figures are estimates from monitoring data; site name removed.
