Solar ESS Co. Ltd.
53 Moo 2 Tambon Nanglae, Amphoe Muang
Chiang Rai 57100, Thailand
Tel 063 151 6694, 089 632 5829
www.solaress.org · LINE: solaress1

SOLAR ESS MONTHLY REPORT · OCTOBER 2026 · SOLISCLOUD · PLANT REPORT


Upgrade opportunity

Laundromat, Songkhla


Add 4 kWp panels

5.8 kWp · 10 kW 3-phase hybrid inverter · battery

538	3.87	84%	4.4	46	11.5
kWh solar	kWh/kWp/day	solar share of use	kWh/day bought	kWh exported	kWh/day from battery

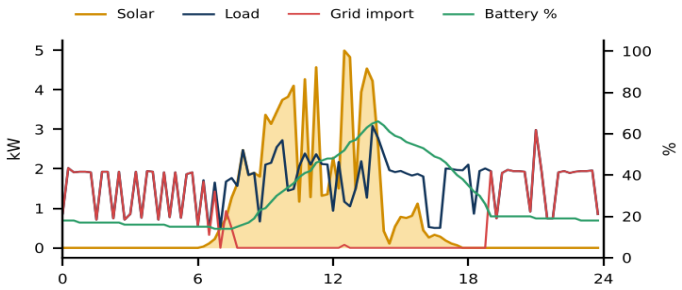

24 October, 5-minute data

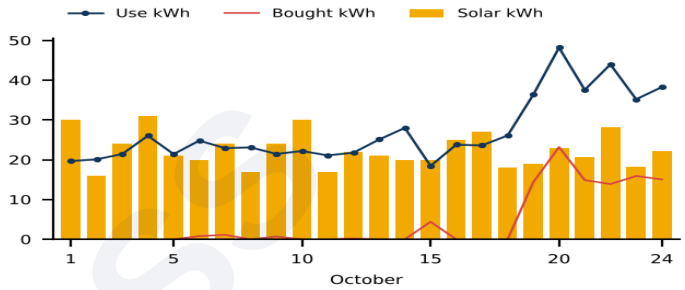

Daily totals, 1–24 October


What we found

- 5.8 kWp on a 10 kW inverter (DC/AC 0.58); battery never gets above 66%.
- Buys 3 kW at night; 84% solar share.
- Also listed on Huawei FusionSolar with 0 kWp – duplicate plant.

What to do

- Add about 4 kWp of panels (inverter has room): about +450 kWh/month.
- Remove or merge the duplicate Huawei listing.

How this plant compares with the other SolisCloud plants (kWh per kWp per day, 1–24 Oct)

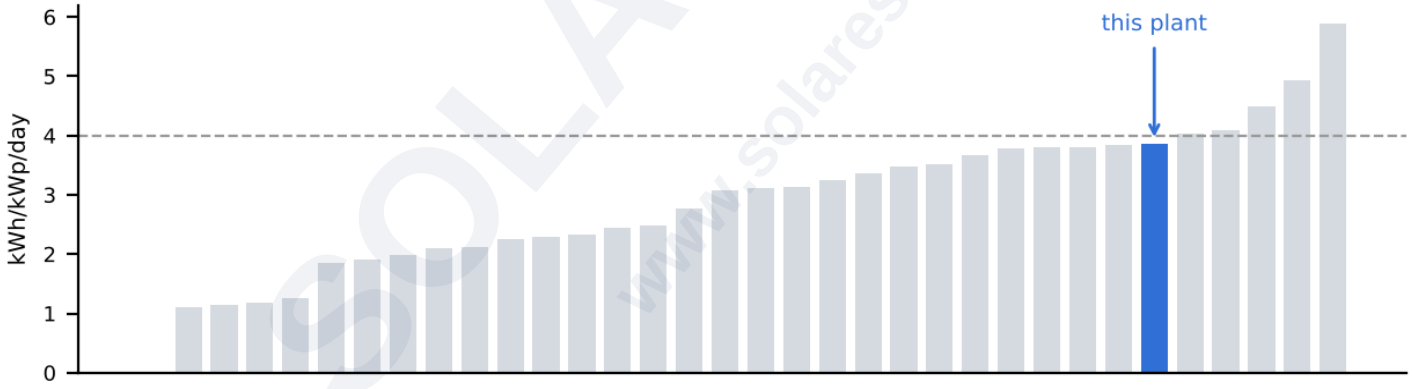

Rank 6 of 34 for yield per kWp. Dashed line ≈ 4.0, a typical clear month in the north and centre. A low yield is not always a fault – a full battery or little daytime load makes the inverter throttle the panels.

This plant report is part of the October 2026 SolisCloud fleet review on www.solaress.org (Technical → Monthly Report), which also lists the recommended standard settings. Figures are estimates from monitoring data; site name removed.
