Solar ESS Co. Ltd.
53 Moo 2 Tambon Nanglae, Amphoe Muang
Chiang Rai 57100, Thailand
Tel 063 151 6694, 089 632 5829
www.solaress.org · LINE: solaress1

SOLAR ESS MONTHLY REPORT · OCTOBER 2026 · SOLISCLOUD · PLANT REPORT


Healthy

Home S7, Shan State (Myanmar)


92% solar

10.24 kWp · 8 kW 1-phase hybrid inverter · battery

600	2.44	92%	2.2	0	11.2
kWh solar	kWh/kWp/day	solar share of use	kWh/day bought	kWh exported	kWh/day from battery

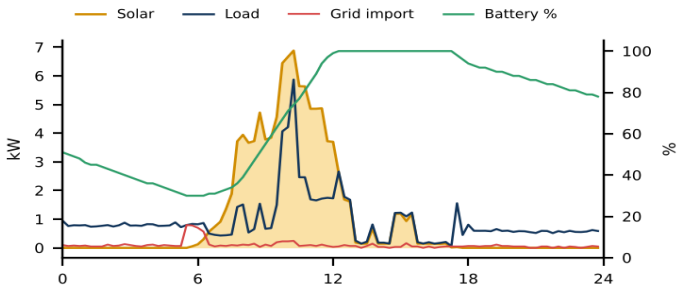

24 October, 5-minute data

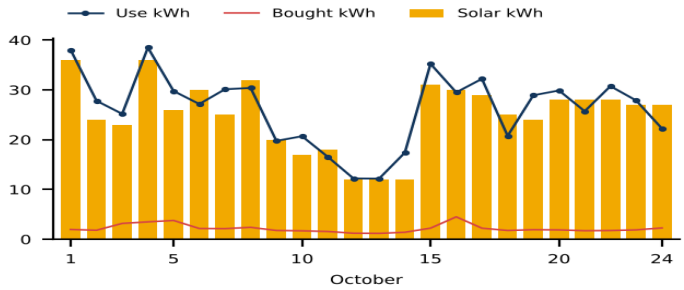

Daily totals, 1–24 October


What we found

• 92% solar share. Time zone UTC+06:30 is correct for Shan State, Myanmar.
• Battery full by 12:00, then solar throttled; 10.24 kWp on 8 kW inverter.

What to do

• No action; daytime loads could use the afternoon surplus.

How this plant compares with the other SolisCloud plants (kWh per kWp per day, 1–24 Oct)

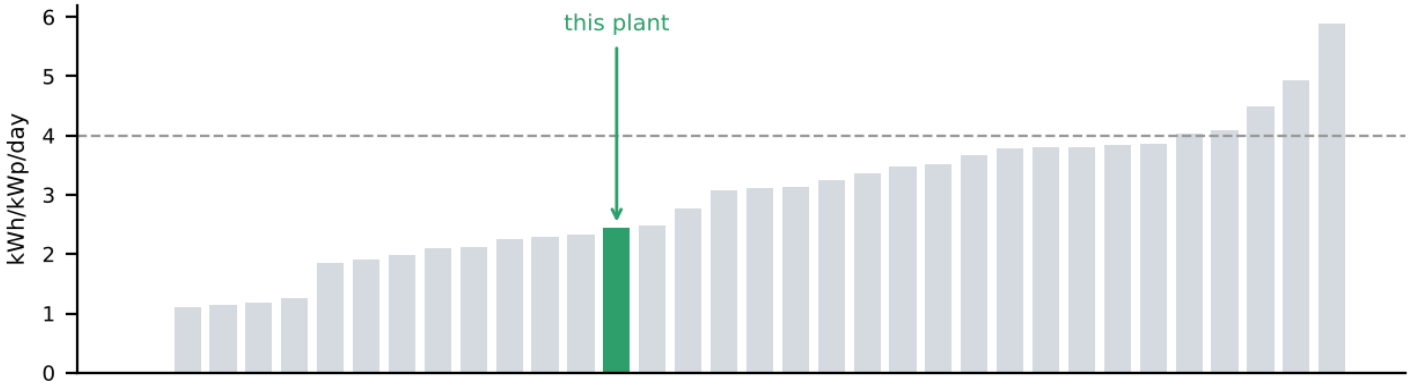

Rank 21 of 34 for yield per kWp. Dashed line ≈ 4.0, a typical clear month in the north and centre. A low yield is not always a fault – a full battery or little daytime load makes the inverter throttle the panels.

This plant report is part of the October 2026 SolisCloud fleet review on www.solaress.org (Technical → Monthly Report), which also lists the recommended standard settings. Figures are estimates from monitoring data; site name removed.
