Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

MONTHLY REPORT · SOLISCLOUD FLEET

CT and battery review: 10 plants

1 October – 8 November 2026 · published 9 November 2026 · all site names removed


SUMMARY

Plant	kWp	Solar kWh/day	kWh/kWp	Import kWh/day	Battery in / out	Status
Resort, Chiang Rai	30.0	112	3.7	197	0.0 / 0.0	Meter fault
Café, Chiang Rai	23.2	69	3.0	29	16.1 / 17.8	Adjust
Hillside home, Chiang Rai	17.8	12	0.7	14	1.0 / 1.3	Fix setting
Residence, Bangkok	20.0	59	3.0	96	0.0 / 0.0	Opportunity
Farm, Trang	10.0	24	2.4	14	12.8 / 11.3	Good
Workshop, Songkhla	20.0	25	1.2	7	2.8 / 1.6	Adjust
House, Lamphun	8.0	30	3.7	19	11.6 / 10.6	Good
Restaurant, Pathum Thani	24.0	50	2.1	181	0.0 / 0.0	Check / clean
Care home, Lampang	25.1	91	3.6	155	0.0 / 0.0	Healthy
Home business, Samut Songkhram	20.1	65	3.2	63	25.9 / 26.4	Best performer

SOLAR ESS www.solaress.org

Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

SOLAR YIELD BY PLANT

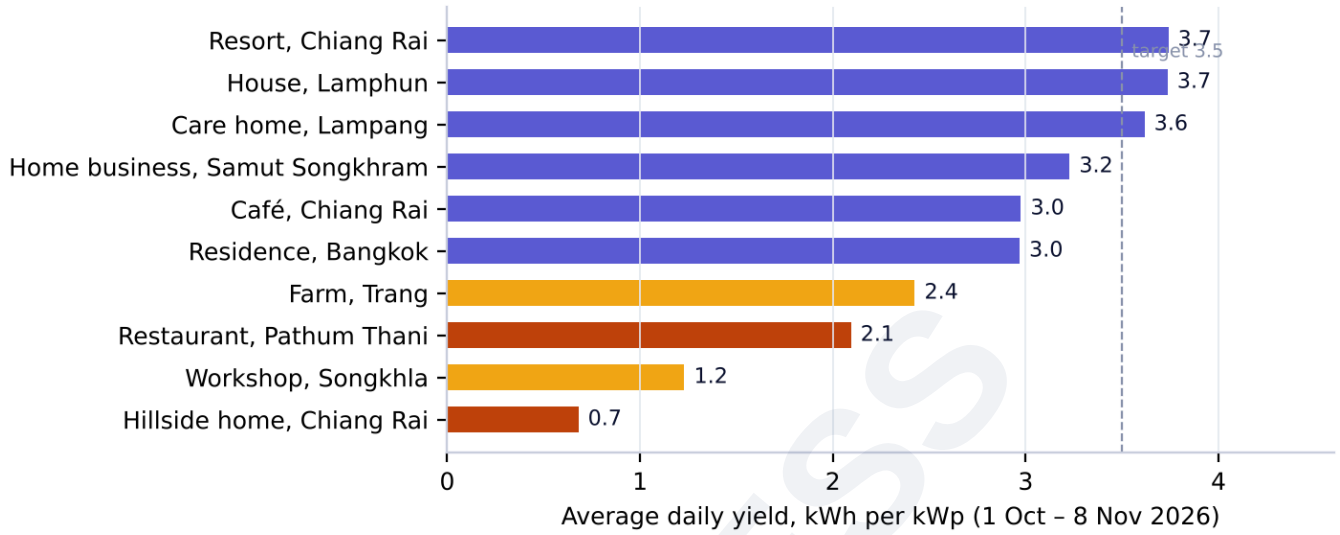

PRIORITY ACTIONS

- **Resort, Chiang Rai:** the grid import counter misses about 60%; check meter CT ratio and all three phases.
- **Hillside home:** battery held at 96–100%; switch to Self-Use with 50% blackout reserve.
- **Restaurant:** low yield (2.1 kWh/kWp); clean and inspect panels, confirm export limit.
- **Café and workshop:** battery floor to 20%.

HOW THIS REVIEW WAS DONE

Daily energy (solar, grid import and export, load, battery charge and discharge) for every day from 1 October to 8 November, plus 5-minute power and battery level curves for 5 and 8 November, from SolisCloud. A CT is judged correct when solar + import − export + battery out − battery in matches the load every day and the import/export sign follows the solar curve.

Next: the setting changes will be applied and the results reported in a follow-up review.

SOLAR ESS
www.solaress.org


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

1. Resort, Chiang Rai


Meter fault


30.0 kWp · three-phase · no battery

112	3.7	602	197	0.0 / 0.0
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

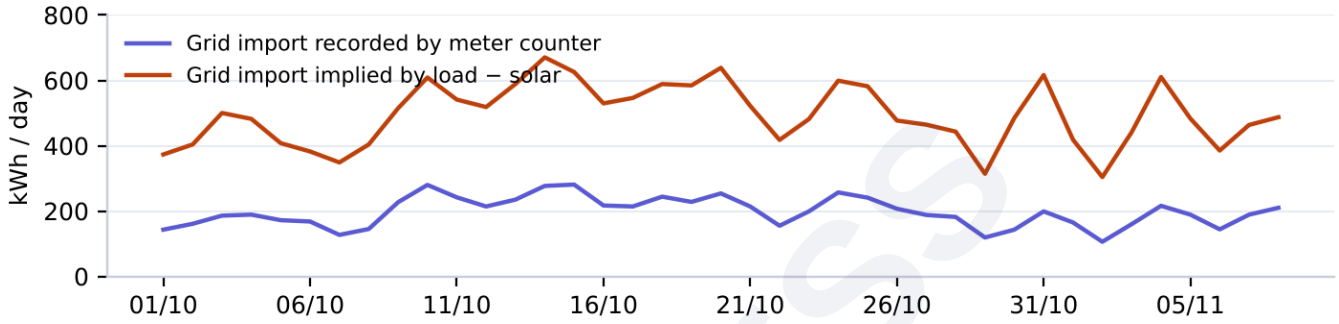

Recorded grid import vs the import implied by load minus solar: the counter misses about 60%.

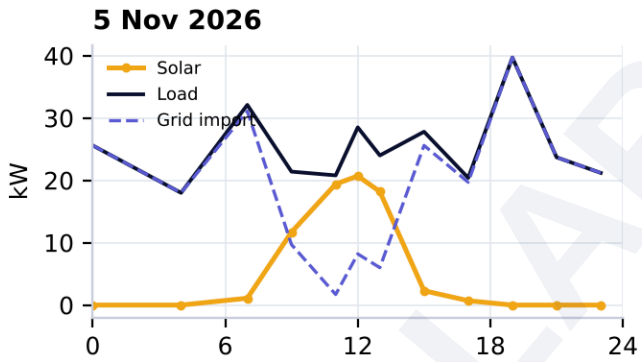

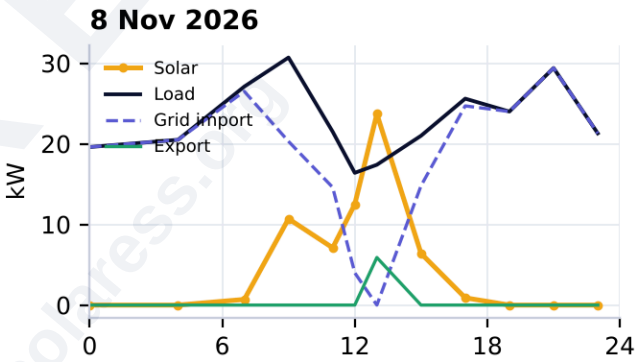

CT / METER

Grid import is under-recorded. Live power readings show 20–30 kW drawn from the grid all night (roughly 480+ kWh a day), but the daily import counter shows only about 197 kWh. Site load therefore appears as about 600 kWh a day against only about 310 kWh of solar plus recorded import. Instant power and its import/export sign look right; the energy counter does not.

BATTERY

No battery installed.

SUGGESTED ADJUSTMENT

- Check the meter's CT ratio setting and that all three phase CTs are connected and the right way round; the counter is probably recording one phase only.
- Compare with the utility bill: whole-site use should be about 14,000 kWh a month.
- Correct the plant type on the monitoring platform (storage → on-grid). Site inspection scheduled.


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

2. Café, Chiang Rai


Adjust


23.2 kWp · 15 kW three-phase hybrid · LiFePO4 battery

69	3.0	100	29	16.1 / 17.8
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

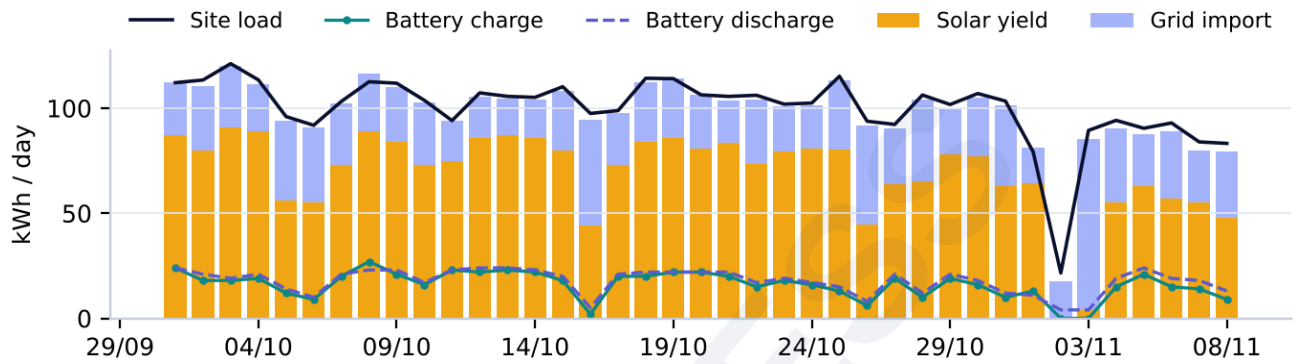

Daily energy 01 Oct – 08 Nov 2026

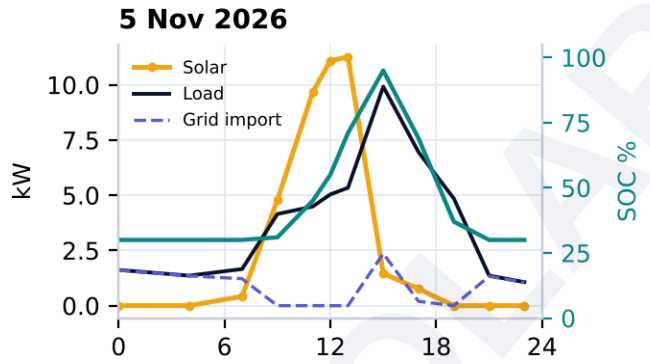

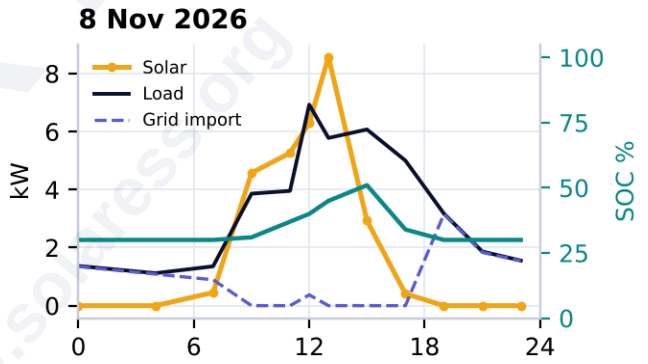

CT / METER

Correct. Grid, load and battery readings balance every day and zero export works (0 kWh exported).

BATTERY

Cycles 16–18 kWh a day. Floor 30%; reaches 55–96% by mid-afternoon and is empty by about 21:00, then the site buys 1–1.6 kW until morning. No solar on 2–3 Nov: planned maintenance shutdown.

SUGGESTED ADJUSTMENT

- Lower the battery floor (overdischarge SOC) from 30% to 20%: about 10% more battery in the evening, safe for LiFePO4.
- Keep Self-Use mode.


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

3. Hillside home, Chiang Rai


Fix setting


17.8 kWp · hybrid · 16 kWh LiFePO4 battery · data from 27 Oct

12	0.7	19	14	1.0 / 1.3
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

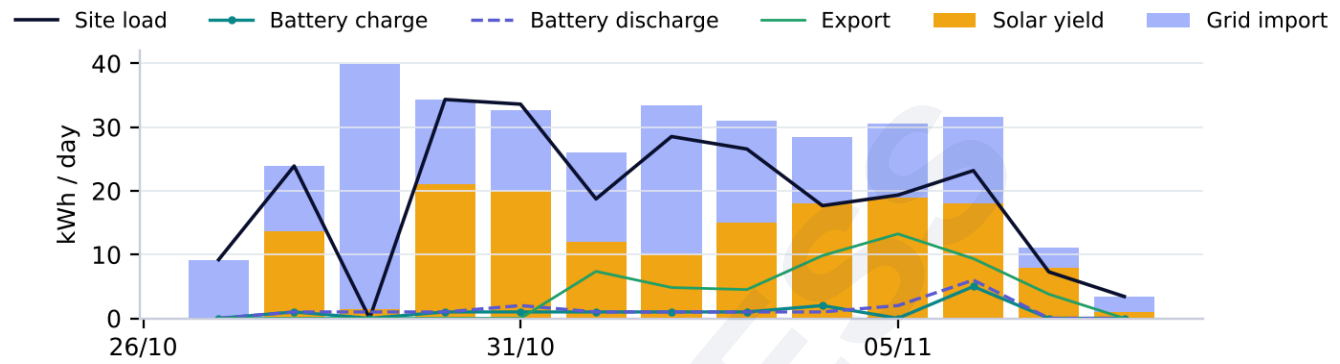

Daily energy 27 Oct – 08 Nov 2026 (false 194 kWh export on 29 Oct left out)

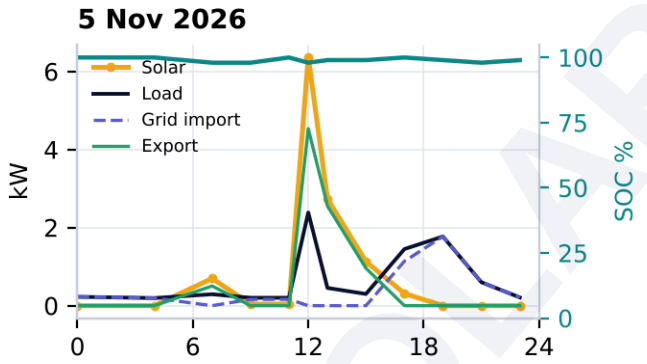

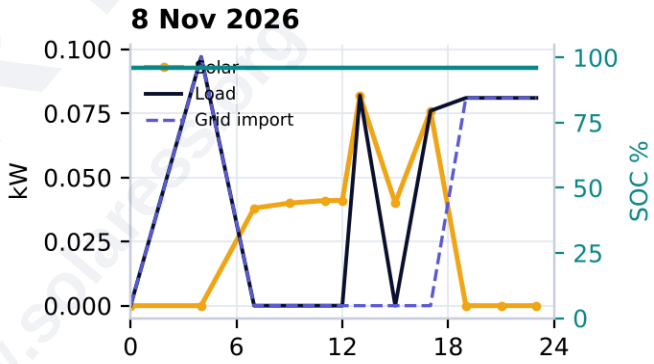

CT / METER

Correct sign and balance, except one false export reading of 194 kWh on 29 Oct (left out of this report).

BATTERY

Battery held full. It stays at 96–100% and moves only about 1 kWh a day. The house exports 4–13 kWh a day and buys about 14 kWh at night. The near-zero solar on 7–9 Nov is the inverter cutting output back (battery full, no export, house almost empty), not a panel fault.

SUGGESTED ADJUSTMENT

- Switch to Self-Use and keep 50% of the battery as blackout reserve; force-charge off. The owner keeps backup power and uses the other half every night (about 6–8 kWh).
- Option: one more 16 kWh battery, so the same 50% reserve covers most nights fully and backup doubles.


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

4. Residence, Bangkok


Opportunity


20 kWp · three-phase · no battery

59	3.0	155	96	0.0 / 0.0
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

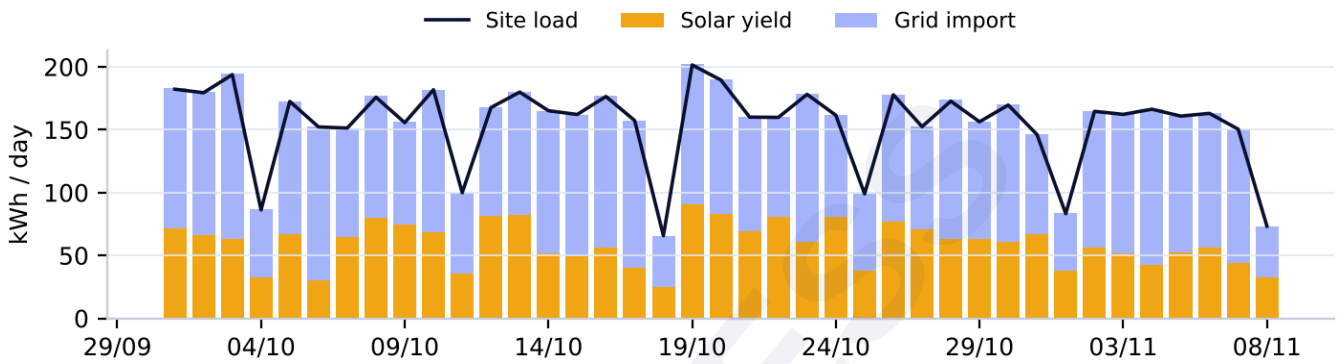

Daily energy 01 Oct – 08 Nov 2026

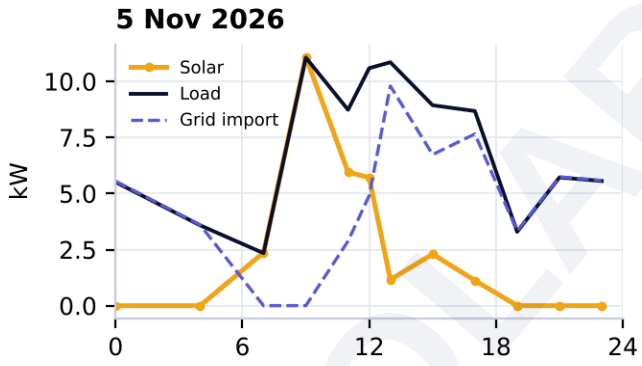

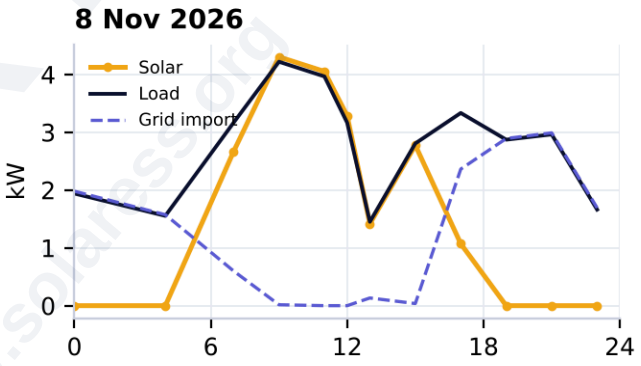

CT / METER

Correct. Zero export works (under 1 kWh a day). In the morning solar exactly follows the load: zero export is holding solar back.

BATTERY

No battery.

SUGGESTED ADJUSTMENT

- With a net-billing contract, allow export to stop wasting morning solar.
- Otherwise add a battery to store the solar now held back.

SOLAR ESS www.solaress.org


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

5. Farm, Trang


Good


10 kWp · hybrid · LiFePO4 battery

24	2.4	37	14	12.8 / 11.3
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

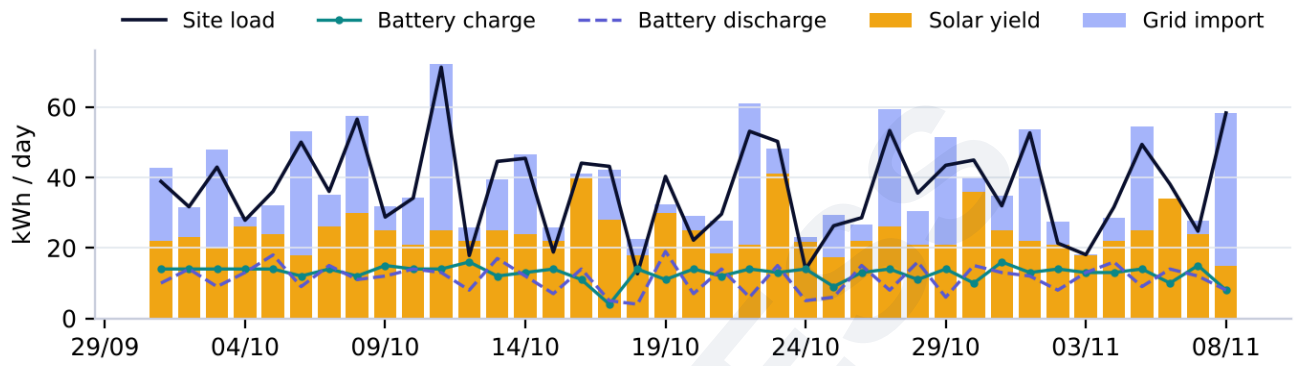

Daily energy 01 Oct – 08 Nov 2026

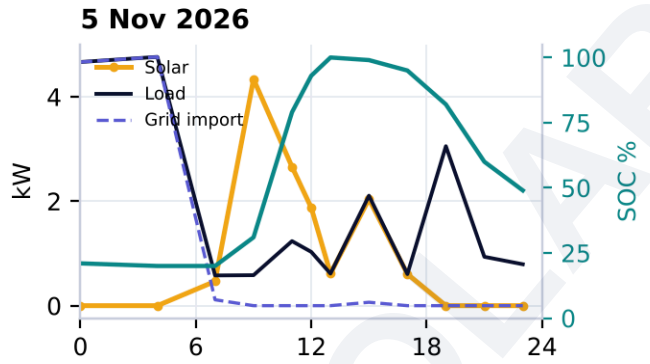

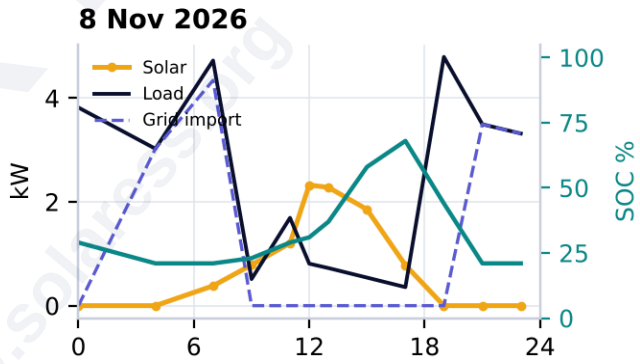

CT / METER

Correct. Balance holds every day; no export.

BATTERY

Floor 20%. On sunny days full by about 13:00, after which solar is held back; empty by about 21:00, then 3–5 kW from the grid overnight. Charge 12.8 / discharge 11.3 kWh a day (88% round trip).

SUGGESTED ADJUSTMENT

- Move daytime loads (pumps, water heater) into 13:00–16:00.
- Or add another 16 kWh battery for the night.


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

6. Workshop, Songkhla


Adjust


20 kWp · hybrid · battery online since 2 Nov

25	1.2	31	7	2.8 / 1.6
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

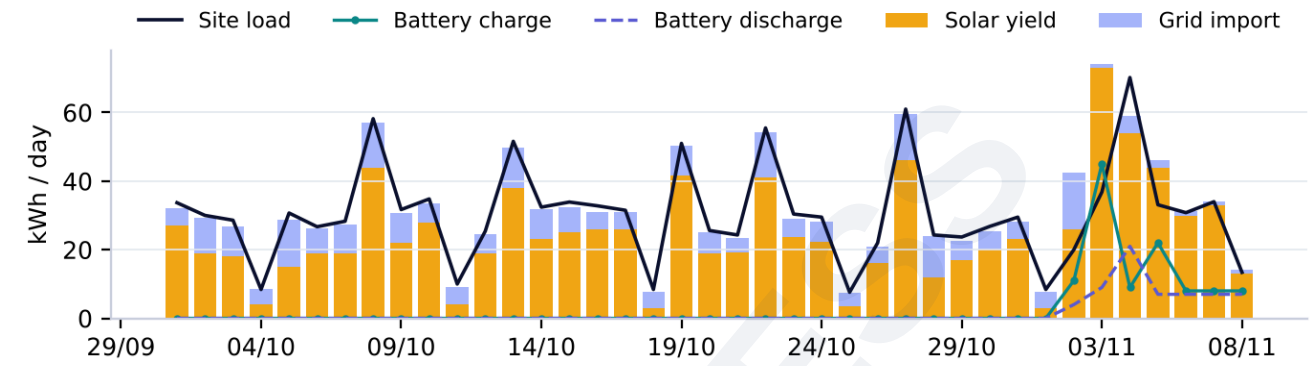

Daily energy 01 Oct – 08 Nov 2026

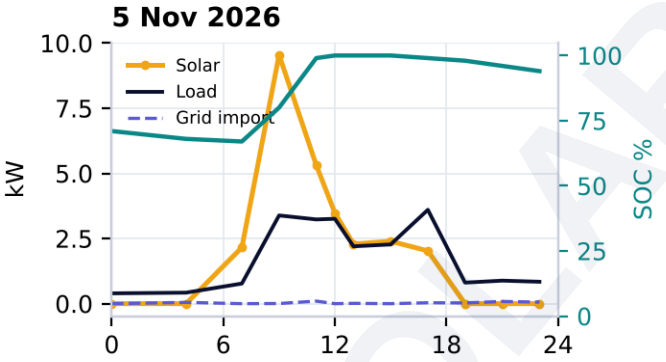

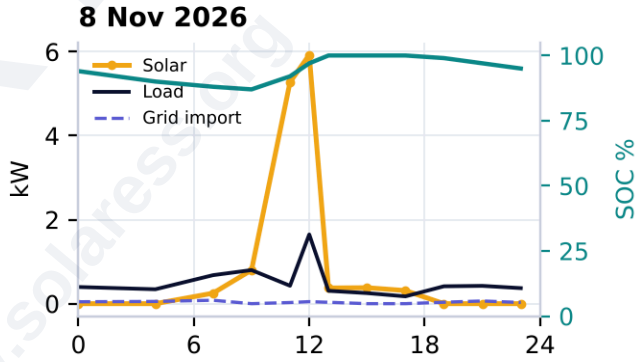

CT / METER

Correct. Grid stays close to zero day and night; zero export works.

BATTERY

Battery online since 2 Nov. Stays between 66% and 100%: full by about 12:00, night load only about 0.4 kW. Solar is cut back after noon, which is why yield is only 1.2 kWh/kWp.

SUGGESTED ADJUSTMENT

- Battery floor 20%, Self-Use.
- Charge the forklifts between 11:00 and 15:00 to use solar that is now wasted.
- With a net-billing contract, allow export.


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

7. House, Lamphun


Good


8 kWp · hybrid · LiFePO4 battery

30	3.7	48	19	11.6 / 10.6
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

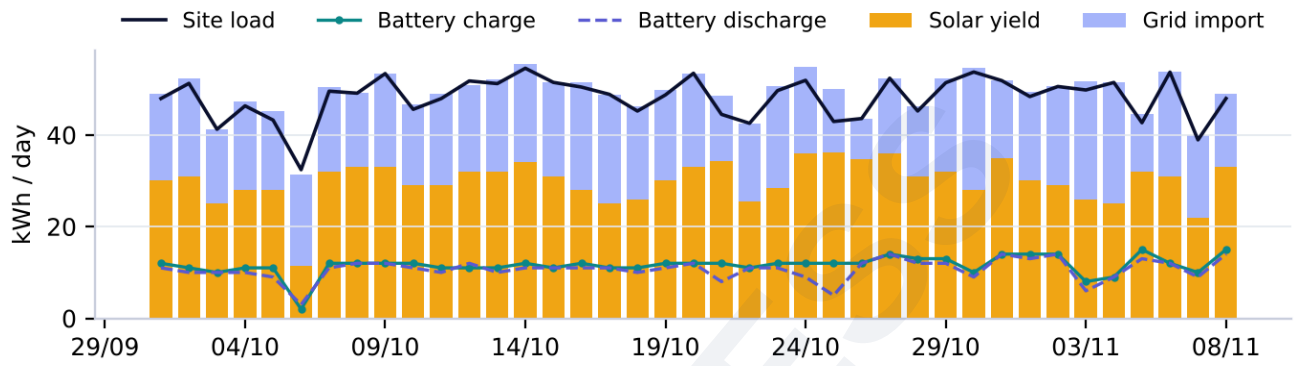

Daily energy 01 Oct – 08 Nov 2026

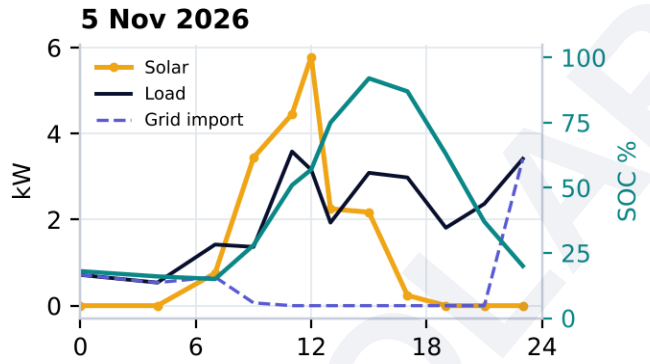

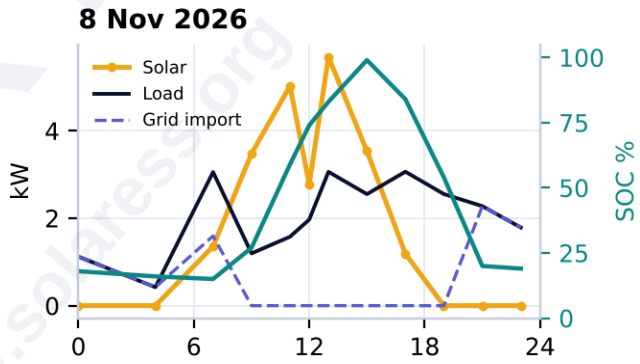

CT / METER

Correct. Balance holds every day; no export.

BATTERY

Floor 15%. Full by about 15:00, empty by about 21:00, then 1.5–3.5 kW from the grid. Charge 11.6 / discharge 10.6 kWh a day (92% round trip). Joint-best yield (3.7 kWh/kWp).

SUGGESTED ADJUSTMENT

- Move daytime loads into the afternoon.
- Or add another 16 kWh battery.

SOLAR ESS www.solaress.org


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

8. Restaurant, Pathum Thani


Check / clean


24 kWp · three-phase · no battery

50	2.1	230	181	0.0 / 0.0
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

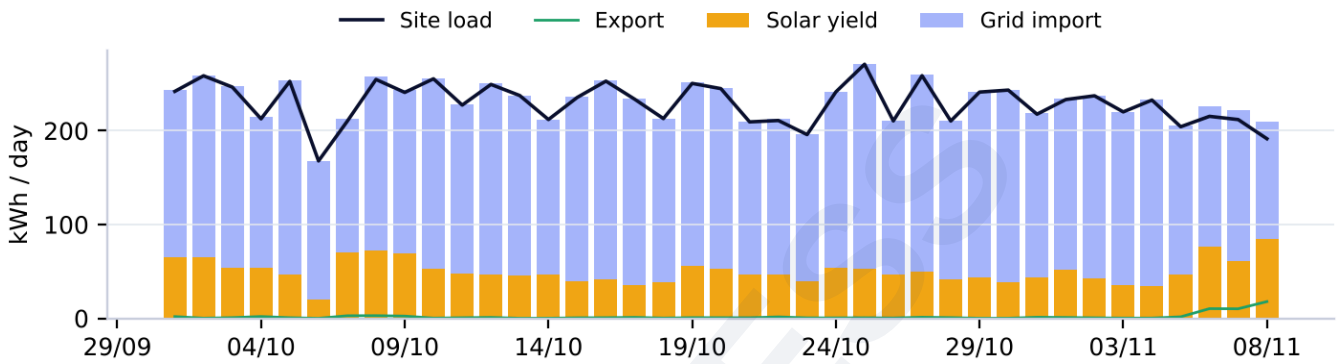

Daily energy 01 Oct – 08 Nov 2026

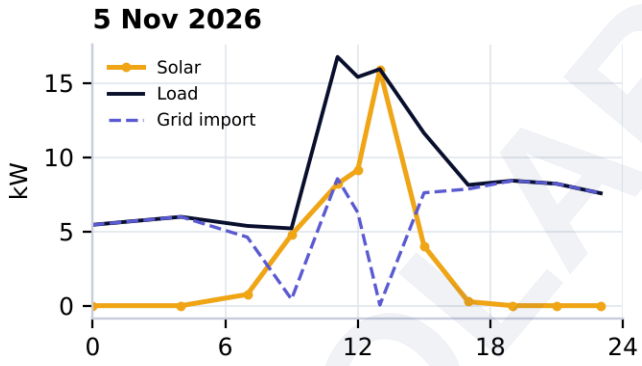

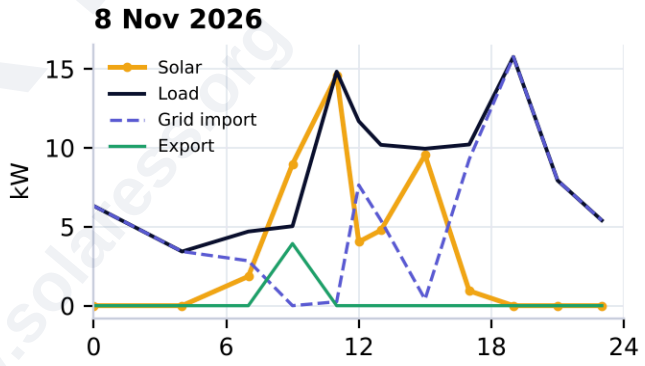

CT / METER

Correct sign. Export rose from about 1 to 10–18 kWh a day from 6 Nov: check whether the export limit was changed.

BATTERY

No battery.

SUGGESTED ADJUSTMENT

- Yield only 2.1 kWh/kWp against 3.6 at the care home. Daytime load is always above solar, so export limits are not the cause.
- Clean and inspect the panels: cooking smoke and grease are likely; check shading and strings.
- Confirm the export-limit setting.

SOLAR ESS www.solaress.org


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

9. Care home, Lampang


Healthy


25.1 kWp · three-phase · no battery

91	3.6	246	155	0.0 / 0.0
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

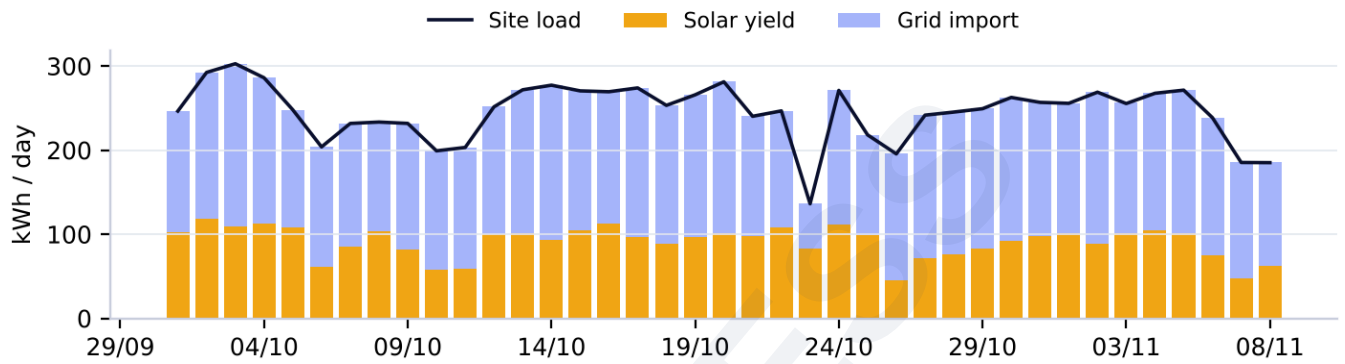

Daily energy 01 Oct – 08 Nov 2026

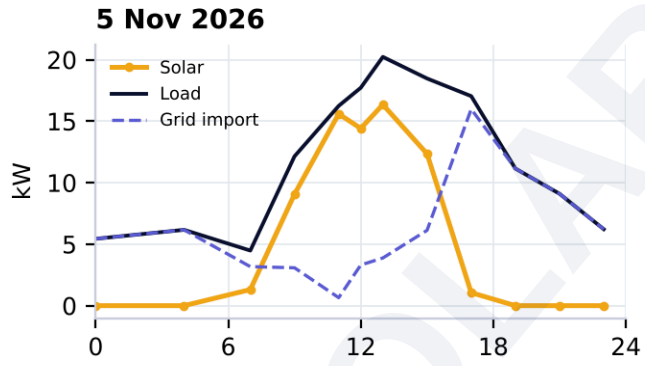

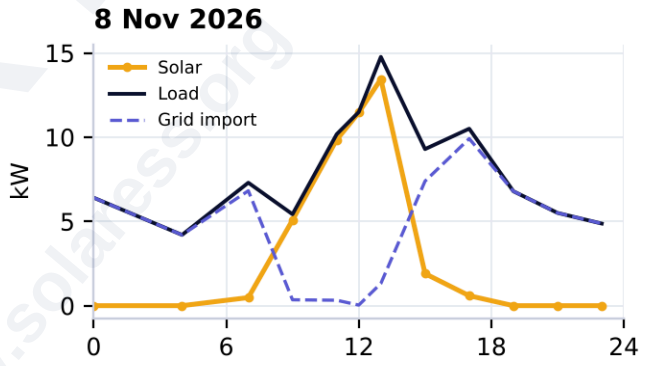

CT / METER

Correct. Balance holds; almost no export.

BATTERY

No battery. Load is above solar all day, so nothing is wasted. Evening peak about 16 kW at 17:00.

SUGGESTED ADJUSTMENT

- No change needed.
- Optional: a battery would cut the evening peak.

SOLAR ESS www.solaress.org


Solar ESS Co. Ltd.
53 Moo 2, Tambon Nanglae, Amphoe Muang, Chiang Rai 57100
Tel 063 151 6694 · 089 632 5829
www.solaress.org · www.โซลาร์เอสส์.com

10. Home business, Samut Songkhram


Best performer


20.1 kWp · hybrid · about 30 kWh usable battery

65	3.2	128	63	25.9 / 26.4
kWh solar / day	kWh per kWp / day	kWh load / day	kWh grid import / day	kWh battery in / out

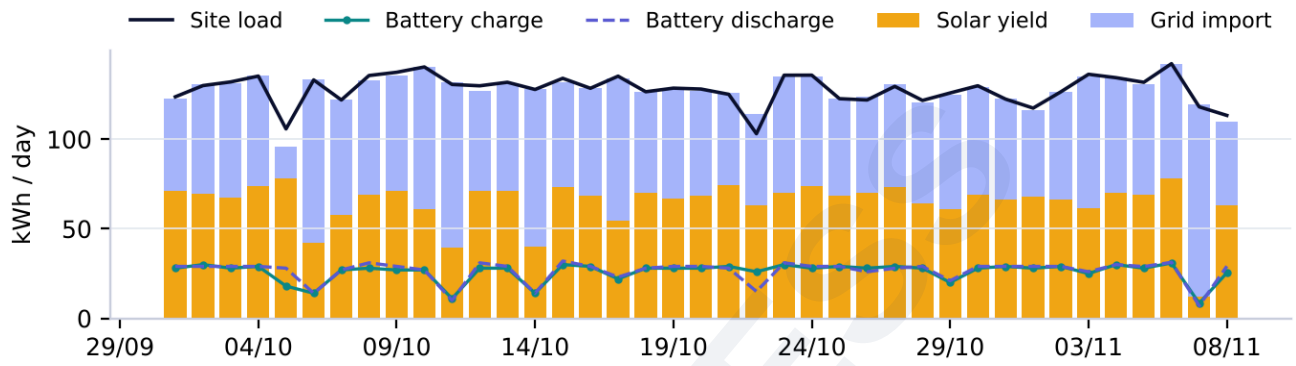

Daily energy 01 Oct – 08 Nov 2026

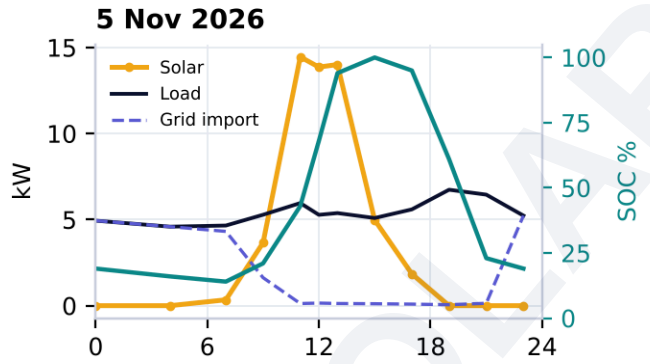

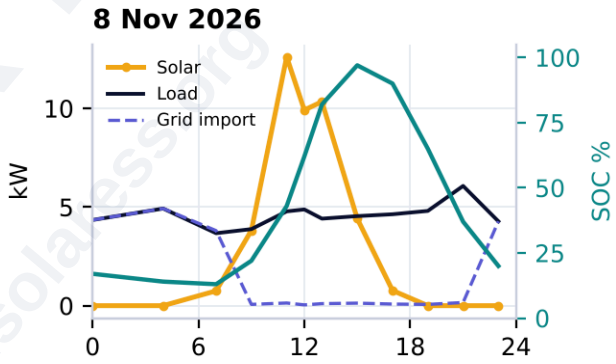

CT / METER

Correct. Grid near zero from 09:00 to about 22:00.

BATTERY

Cycles fully every day (about 26–29 kWh): full by about 15:00, down to about 19% by 23:00, then about 4.5 kW from the grid until morning.

SUGGESTED ADJUSTMENT

- No setting change needed: already close to optimal.
- On a TOU tariff the night import is already in cheap off-peak hours; on a flat tariff the only gain is more battery plus a few more panels.

SOLAR ESS www.solaress.org
